

Exam Questions PRINCE2-Practitioner

PRINCE2 Practitioner exam

<https://www.2passeasy.com/dumps/PRINCE2-Practitioner/>



NEW QUESTION 1

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company’s development team. All course materials will

be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company’s IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company’s document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

ABC Company uses a standard development model to develop courses and uses PRINCE2 to manage these projects. The objectives from the Health and Safety Training Project have been documented in the business plan of ABC Company. This business plan has triggered this project. As a result, to save time, the executive has decided to simplify the ‘starting up a project’ process. The project mandate will be adapted and becomes the project brief.

Is this appropriate, and why?

- A. Yes, because the business outcomes are clear, the project brief can be a sample statement elaborating the mandate.
- B. Yes, because the executive can initiate the project based on the project mandate by passing the ‘starting up a project’ process.
- C. No, because the project brief should be a statement which includes a fuller description of the project.
- D. No, because capturing lessons from previous projects identify lessons to be applied to this project.

Answer: C

NEW QUESTION 2

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company’s development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will

use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information. RISK

The project is in stage 2. The project manager has heard that a competitor may launch a similar e-learning course much sooner than ABC Company. There is a threat that the earlier launch of a competitor's course may reduce the profitability of ABC Company training courses.

Here are three responses to this risk. Which risk response type (A-F) are they?

Choose only one response type for each risk response. Each response type can be used once, more than once, or not at all.

Avoid a threat	Record the risk in the risk register and monitor the competitor's activities.
Reduce a threat	Deliver the health and safety training course earlier than originally planned.
Transfer the risk	Continue with the delivery of the project, as planned, because ABC Company's courses are believed to be on higher quality.
Accept the risk	
Prepare contingent plans	
Enhance an opportunity	

- A. Mastered
B. Not Mastered

Answer: A

Explanation:



NEW QUESTION 3

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to

projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information. STARTING UP A PROJECT

Here are three actions carried out during the 'starting up a project' process. As part of which activity (A-F) should each action occur?


Choose only one activity for each action. Each activity can be used once, more than once, or not at all.

Appoint the executive and the project manager	Agree whether IT department of ABC Company has the skills and capacity to deliver the 'e-learning course' or whether it should be delivered by an external supplier.
Capture previous lessons	Discuss the need for the health and safety training, in order to identify who would be a suitable candidate to manage the Health and Safety Training Project.
Design and appoint the project management team	Define the reporting and control arrangements based on the lessons from the most recently completed training design and delivery project.
Prepare the outline business case	
Select the project approach and assemble the project brief	
Plan the initiation stage	

- A. Mastered
- B. Not Mastered

Answer: A

Explanation:

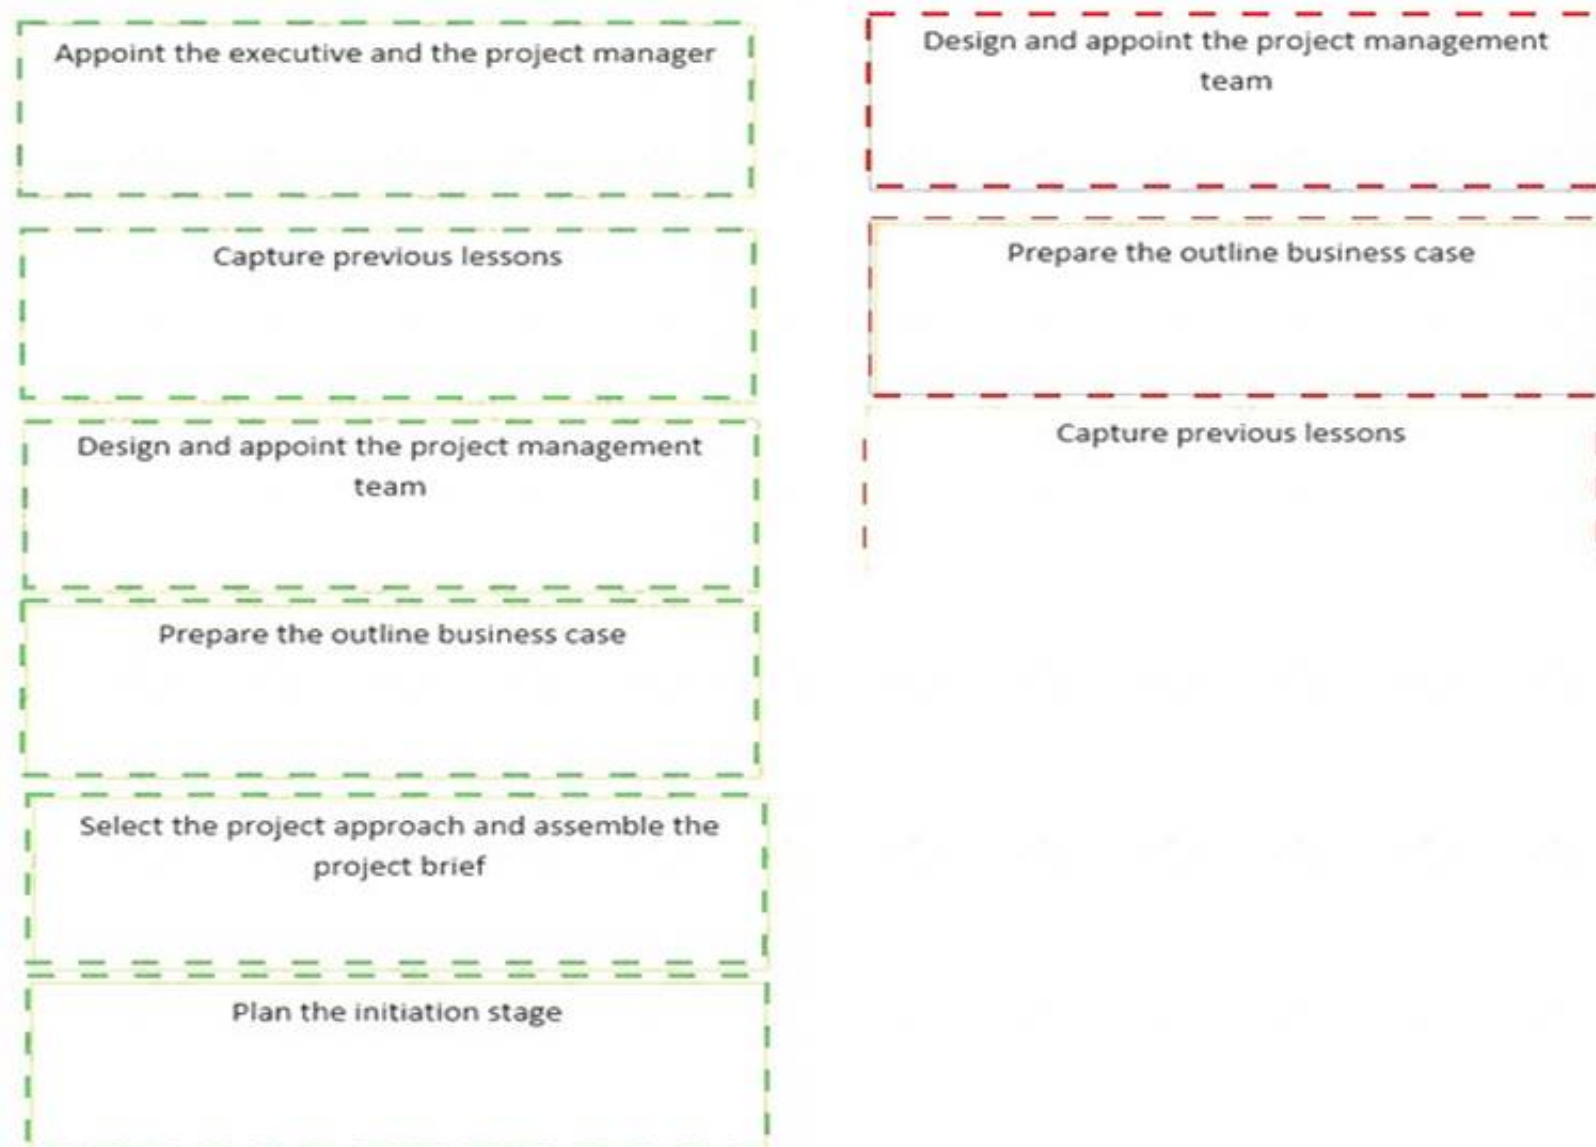

NEW QUESTION 4

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company’s development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company’s IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in

accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

The executive has set the following tolerances for stage 2: Time (+/- 1 week)

Cost (+/- £20,000)

Scope (using MoSCoW prioritization technique)

Risk (based on the risk appetite defined in the risk management approach)

These tolerances have been recorded in the stage plan. The project manager will report progress regularly via highlight reports to the project board and use exception reports to raise exceptions. In addition, the project assurance role will monitor the stage to provide confidence to the project board that exceptions are being reported.

How well does this apply the 'manage by exception' principle, and why?

- A. It applies the principle well, because tolerances should be set for the related aspects of project performance for each stage.
- B. It applies the principle well, because the project manager needs to control the project using discrete management stages.
- C. It applies the principle poorly, because tolerances should be set for each stage against each of the six aspects of project performance.
- D. It applies the principle poorly, because it is the regular reporting of progress that should give the project board the required confidence.

Answer: C

NEW QUESTION 5

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.
 End of the additional information.

In order for ABC Company to achieve the expected sales of the health and safety training course, the senior user will need to ensure that all staff understand the objectives and target audience for the course. In addition, these sales will need to be added to each individual's sales targets. These activities have been included in the benefits management approach.

Is this appropriate, and why?

- A. Yes, because how the benefits will be measured needs to be documented.
- B. Yes, because the actions required to achieve the outcomes need to be documented.
- C. No, because the expected sales increase should be recorded in the business case.
- D. No, because actions to deliver the outputs should be recorded in the stage plan.

Answer: A

NEW QUESTION 6

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

During stage 4, a work package was authorized for the 'delivered pilot courses' to be completed by the end of week 2. The 'finalized materials' work package will start in week 3. Both work packages have zero tolerances, and finalizing the materials is dependent on feedback from the pilot courses.

During week 1, there were some problems with the pilot courses, so at the start of week 2 the team manager rescheduled the courses to week 3, and reported this in the weekly checkpoint report as the end of week 2.

Should the team manager have reported this delay previously as an issue, and why?

- A. Yes, because the work package to deliver the pilot courses was forecast to exceed its time tolerance.
- B. Yes, because a team manager should not change the scheduled order of a work package.
- C. No, because the checkpoint report for week 1 should include information on any issues that occurred.
- D. No, because the feedback from the rescheduled courses can be used in week 4 to finalize the materials.

Answer: C

NEW QUESTION 7

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company’s development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company’s IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company’s document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information. PLANS

Here are three events to managing plans for the project.

In which management product (A-E) should the result of each event be recorded?

Choose only one product for each event. Each product can be used once, more than once or not at all.


Project plan	The project manager instructs the team manager to take corrective action, which will keep costs within the overall project and stage tolerances.
Stage plan	The operations Director tells the project manager during stage 3, that 50% of the Learn-it trainers have been accredited. The remainder will be accredited within the agreed tolerances.
Team plan	The project manager is instructed to produce a replacement plan to the current stage, to be presented to the project board at a meeting the following week.
Exception plan	
Work package	
Project product description	

- A. Mastered
- B. Not Mastered

Answer: A

Explanation:

The project manager instructs the team manager to take corrective action, which will keep costs within the overall project and stage tolerances.	Project plan
The operations Director tells the project manager during stage 3, that 50% of the Learn-it trainers have been accredited. The remainder will be accredited within the agreed tolerances.	Stage plan
The project manager is instructed to produce a replacement plan to the current stage, to be presented to the project board at a meeting the following week.	Team plan
	Exception plan
	Work package
	Project product description



NEW QUESTION 8

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

During stage 3, the operational staff that handle course bookings asked for the project scope to be increased for an online booking function. The additional product has been as it will enable them to process bookings more quickly and accurately.

Is this an appropriate application of the ‘focus on products’ principle, and why?

- A. Yes, because the goal is to seek opportunities to implement improvements after the life of the project.
- B. Yes, because the project needs to fulfill stakeholder expectations by delivering the products required.
- C. No, because there needs to be an understanding of the products from the start of the project.
- D. No, because existing product descriptions provide a means to estimate effort to planning.

Answer: B

NEW QUESTION 9

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information. CLOSING A PROJECT

Benefits relating to income and business reputation after the project has closed cannot be shown at project closure.

Which statement describes how the 'closing a project' process makes provision for this?

- A. As part of the 'prepare planned closure' activity
- B. It will be confirmed that the project has delivered what was defined in the project product description.
- C. As part of the 'prepare planned closure' activity
- D. It will be confirmed that the acceptance criteria defined in the project product description have been met.
- E. As part of the 'hand over products' activity, the benefits management approach will be updated to include future activities for benefit measurement.
- F. As part of the 'hand over products' activity, the 'finalized materials' will be passed to the operational business environments.

Answer: D

NEW QUESTION 10

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

The project's change control approach states that PRINCE2's recommended issue and change control procedure will be used. The senior user has requested that a new set of marketing materials and marketing channels be introduced to support the launch of the training course. The senior user has suggested that this should be managed informally.

Where should the project manager record the issue, and why?

- A. In the daily log, because a change to a product at the default level can be handled informally.
- B. In the daily log, because the senior user has advised that this change should be informally.
- C. In the issue register, because this is a request for change requiring a change to a baseline.
- D. In the issue register, because issues should be recorded here first, before determining how to manage them.

Answer: D

NEW QUESTION 10

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

The project is now closed. The expected increase in revenue is not being achieved. It has been agreed with the team manager for the 'marketing materials' that additional marketing activities will be undertaken to achieve the expected increase in revenue.

Who should be responsible for monitoring the results of the marketing activities, and why?

- A. Senior user, because this person is responsible for realizing the benefits post-project.
- B. Senior user, because this person is responsible for specifying the desired from the project.
- C. The team manager for the 'marketing materials', because this person has the skills to demonstrate that the activities are effective.
- D. The team manager for the 'marketing materials', because the project board is disbanded at the end of the project.

Answer: A

NEW QUESTION 13

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

A construction company that is one of ABC Company's key clients has agreed to provide a member of the staff to review and comment on the 'e-learning course'.

Which stakeholder interest should the member of staff represent, and why?

- A. Supplier, because this stakeholder provides the expertise required by the project.
- B. Supplier, because this stakeholder is an external supplier.
- C. User, because this stakeholder may train its staff using the 'e-learning course'.
- D. User, because this stakeholder ensures that the project provides value for money.

Answer: D

NEW QUESTION 18

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered.

ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information. MANAGING PRODUCT DELIVERY

The team manager for the production of the 'marketing materials' has identified that they will not be ready within the timescale agreed in the work package. The team manager has sufficient tolerance to take corrective action. As a result, additional resources have been assigned to this work package.

Which theme is being applied?

- A. Risk
- B. Organization
- C. Progress
- D. Change

Answer: A

NEW QUESTION 19

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information. MANAGING A STAGE BOUNDARY

The ABC Company trainers have been accredited and the course booking procedures have been amended. The 'managing a stage boundary' process is taking place at the end of stage 3.

Which activity should occur during the 'update the business case' activity?

- A. Update the overall plan with the time and cost taken to develop the 'e-learning course' and 'amended course booking procedures'
- B. Break the 'planned pilot courses' down into component products in order to identify the work required to deliver them.
- C. Review whether the possible sales of the training course to external companies are likely to cover the project costs.
- D. Review whether a new team manager should be appointed to lead the delivery of the pilot courses during stage 4.

Answer: A

NEW QUESTION 24

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages: End of the Project scenario.

Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

The development of the 'e-learning course' will be outsourced to an external supplier and their key members will join the project management team. The supplier wants to keep their work processes confidential and not share these with ABC Company. ABC Company has agreed.

Who should approve the external supplier's team plan?

- A. Senior supplier
- B. Project manager
- C. Supplier assurance
- D. Corporate, programme management or customer

Answer: D

NEW QUESTION 29

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver "capability to provide health and safety training", including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company's development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company's IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company's document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

All the products that are due in stage 3 have been completed, apart from the 'updated corporate quality procedures'. The work has been completed but the product has not yet been approved. The executive has been told that it will be signed off before the end of the project. In response to an exception report, the executive has instructed the project manager to plan to obtain approval of the product in stage 4.

Is this appropriate application of the report management stage end' activity, and why?

- A. Yes, because approval of the product can be carried forward into the next stage, with authority from the project board.
 B. Yes, because the completion of the product in the next stage is a follow-on action recommendation for stage 4.
 C. No, because approval of the products was planned for stage 3 and must be completed before the stage ends.
 D. No, because a project-level exception plan is required before approval of the quality procedures can be delayed.

Answer: A

NEW QUESTION 32

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers.

ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents.

The e-learning course will be developed by a specialist external consultancy. The materials for

classroom-based training will be delivered by ABC Company’s development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses.

The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project.

The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery off all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company’s IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations. Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company’s document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

Use the ‘Additional Information’ in the Scenario Booklet to answer this question.

The Operations Director is the executive for the project and has proposed that a senior course developer be appointed as project manager. The course developer works in the Training Development Manager’s team and has a good understanding of the standard course development model. The course developer was a team manager on a previous project for which the Operations Director was the executive.

Is this proposed appointment appropriate, and why?

- A. Yes, because the course developer is responsible for ensuring that trainers deliver courses to the required standard.
 B. Yes, because the course developer is likely to have the project management and specialist knowledge required.
 C. No, because the course developer’s team reports to the Business Development Director, not the Operations Director.
 D. No, because there is a conflict of interest as the Training Development Manager is responsible for gaining accreditation.

Answer: A

NEW QUESTION 34

- (Exam Topic 1)

Project Scenario – Health and Safety Training Project:

ABC Company is a well-established training company that uses a standard model to develop training materials and deliver courses to customers. ABC Company has commissioned a project in response to recent changes in government legislation relating to health and safety on construction sites. The project will deliver “capability to provide health and safety training”, including the materials needed for classroom-based training and e-learning. The expected benefits for construction companies include a reduction in lost days and legal costs due to accidents. The e-learning course will be developed by a specialist external consultancy. The materials for classroom-based training will be delivered by ABC Company’s development team. All course materials will be piloted before they are used. ABC Company will deliver training to its customers and also hopes to sell the course materials to other training companies as part of their operational business. ABC Company will use their own sales and marketing departments to promote the courses. The legislation requires construction companies to comply with the new legislation within two years. The course materials and trainers have to be accredited by a government agency before courses can be delivered. ABC Company is planning to deliver pilot courses within five months of starting the project. The ABC Company standard development model for new courses recommends the following stages:

Stage 1	Initiation stage
Stage 2	Classroom-based training materials Marketing materials Training venue specifications Accredited classroom-based course
Stage 3	E-learning course Amended course booking procedures Marketed courses Planned pilot courses Updated corporate quality procedures Accredited e-learning course Accredited trainers
Stage 4	Delivered pilot courses Finalized materials Project product: Capability to provide health and safety training

End of the Project scenario. Additional Information:

The Chief Executive Officer (CEO) founded the company five years ago. Under her leadership, ABC Company has grown quickly into a successful training company. It delivers a range of accredited professional training.

The Finance Director is also a founder member of ABC Company and is responsible for authorizing budgets for the Operations and Development Teams. She authorizes all large contracts personally.

The Purchasing Manager reports to the Finance Director and is responsible for managing and monitoring supplier contracts.

The Operations Director is responsible for the delivery of all training and for the training development budget. His department organizes courses, venues and trainers. They work with the Product and the Sales teams to provide a comprehensive training schedule. ABC Company’s IT manager reports to the Operations Director.

The Business Development Director has recently been appointed to identify new training needs and propose new products. She will work with the Operations Director to ensure a cost-conscious approach and that appropriate development technologies are used for the health and safety course.

The Training Development Manager reports to the Business Development Director and is responsible for developing training materials and gaining accreditation, in accordance with the standard course development model. Course developers in his team have skills in a range of development technologies and are allocated to projects as needed.

The Training Delivery Manager, who reports to the Operations Director, is responsible for ensuring that internal and external trainers deliver ABC Company training courses to the required standard. He also checks course materials to ensure they are fit for purpose and of the required quality.

The Central Services Director has responsibility for corporate communications, facilities management and configuration management. He recently led a project to consolidate all company quality systems into one quality management system and set up a corporate quality department, now managed by the Corporate Quality Manager.

The Corporate Document Manager reports to the Central Services Director. She helped establish the company’s document management system and now operates it across the business. She manages a team of administrators and contracts staff when workload is high.

The Sales Director joined ABC Company two months ago and is keen to establish himself by suggesting new markets for the courses and material. All account managers and the marketing team report to him. They promote existing training courses to other training companies and existing customers.

End of the additional information.

ABC Company carried out a similar project two years ago, in response to changes in health and safety legislation for the health service. The experiences from that project were used to refine the corporate risk management policy. For that reason, the project board decided to use the corporate risk management policy in the risk management approach for this project.

Is this appropriate, and why?

- A. Yes, because experience from previous projects should be taken into account in the risk management approach.
- B. Yes, because the corporate risk management policy was updated, as a result of lessons from previous projects.
- C. No, because the risk management approach should be tailored to suit the project and its environment.
- D. No, because a separate risk management approach is not necessary when the company has a risk management policy.

Answer: A

NEW QUESTION 36

- (Exam Topic 2)

Scenario

Additional Information

During the initiation stage the Project Manager met with the Marketing Director to find out more about the requirements of the promotional calendar and recorded the following notes:

There has been a reduction in the order numbers at the MNO Manufacturing due in part to the increased marketing activities of its competitors. 10% of customers have not re-ordered in this financial year and staff morale is poor. A number of skilled staff have left as a result and replacement staff have not been recruited due to the reduced operation. If the project is successful, a recruitment campaign will be required to fill the existing staff vacancies and there may be a requirement for additional staff. Operational costs are likely to increase because skilled staff are expensive and difficult to find.

In financial terms, there were a total of 1,500 orders in the last financial year, each with an average profit of £2k. The Marketing department believes that sending a promotional calendar to our current and prospective customers would increase orders by at least 10% with a minimum of 10 further orders from the list of prospective customers within 12 months from the date of distribution.

The Marketing Director will be funding the project from the business marketing budget. She believes that the effect of a good company image portrayed by a successful calendar would last into a second year. She has forecast the same increase in orders for a second year and predicts that the annual employee satisfaction survey will show a measurable improvement in staff morale.

A number of alternatives were explored, including:

- 20% discount for all repeat customers - not cost-effective and very short term
- A promotional calendar as a free Christmas gift - would target current and prospective customers and the benefits would last into a second year
- A series of television and press advertisements was too expensive
- A direct mail shot to all customers - benefit would be short term
- Creation of an internet website - would not suit all customers

The calendar is seen as the favored option, as long as the company's competitors do not increase their marketing activity. Whilst the Marketing department wants a very high quality, glossy product, the project management team must be aware of the cost this will incur.

Using the Project Scenario and the additional Information provided for this question In the Scenario Booklet, answer the following question.

Which 2 statements should be recorded under the Reasons heading?

- A. The Marketing department believes that sending a promotional calendar to current and prospective customers will increase orders by at least 10%.
- B. 10% of customers have not re-ordered in this financial year.
- C. 1,500 orders are expected, each with an average profit of £2k.
- D. The Marketing department believes that the effect of a good company image, portrayed by a successful calendar, will last into a second year.
- E. MNO Manufacturing is experiencing a fall in orders due in part to the increased marketing activities of its competitors.

Answer: BE

NEW QUESTION 40

- (Exam Topic 2)

Scenario

Additional Information

During the initiation stage the Project Manager met with the Marketing Director to find out more about the requirements of the promotional calendar and recorded the following notes:

There has been a reduction in the order numbers at the MNO Manufacturing due in part to the increased marketing activities of its competitors. 10% of customers have not re-ordered in this financial year and staff morale is poor. A number of skilled staff have left as a result and replacement staff have not been recruited due to the reduced operation. If the project is successful, a recruitment campaign will be required to fill the existing staff vacancies and there may be a requirement for additional staff. Operational costs are likely to increase because skilled staff are expensive and difficult to find.

In financial terms, there were a total of 1,500 orders in the last financial year, each with an average profit of £2k. The Marketing department believes that sending a promotional calendar to our current and prospective customers would increase orders by at least 10% with a minimum of 10 further orders from the list of prospective customers within 12 months from the date of distribution.

The Marketing Director will be funding the project from the business marketing budget. She believes that the effect of a good company image portrayed by a successful calendar would last into a second year. She has forecast the same increase in orders for a second year and predicts that the annual employee satisfaction survey will show a measurable improvement in staff morale.

A number of alternatives were explored, including:

- 20% discount for all repeat customers - not cost-effective and very short term
- A promotional calendar as a free Christmas gift - would target current and prospective customers and the benefits would last into a second year
- A series of television and press advertisements was too expensive
- A direct mail shot to all customers - benefit would be short term
- Creation of an internet website - would not suit all customers

The calendar is seen as the favored option, as long as the company's competitors do not increase their marketing activity. Whilst the Marketing department wants a very high quality, glossy product, the project management team must be aware of the cost this will incur.

Using the Project Scenario and the additional Information provided for this question In the Scenario Booklet, answer the following question.

Which 2 statements should be recorded under the Business options heading?

- A. Produce a promotional calendar as a free Christmas gift to current and prospective customers.
- B. Use a professional photographer to create the photographs for the calendar.
- C. Create the photographs for the calendar internally.
- D. Outsource the creation of the calendar to a professional marketing company.
- E. Do nothing.

Answer: AE

NEW QUESTION 42

- (Exam Topic 2)

Scenario

A central government department, the Ministry of Food Hygiene (MFH), faces increasing pressure to cut costs, better manage suppliers' performance and reduce the confusion caused by inadequate internal controls, outdated standards and outdated technology. External consultants were employed to conduct a feasibility study to identify options to address the problems, and the likely costs and benefits. The following options were considered:

Do nothing.

Re-engineer selected business functions. Outsource selected business functions.

The feasibility study concluded that there was a case for outsourcing the MFH Information Technology Division and the Facilities Division (maintenance of buildings and grounds). The recommendations were:

One service provider should be contracted to provide the services currently provided by the Information Technology Division and the Facilities Division.

A 10-year service contract should be agreed with the selected service provider.

The feasibility study developed high-level designs of the current organization, processes, systems and operating models, plus an outline Business Case for the required project. The external consultants also made the following recommendations for the management of the project:

Use PRINCE2.

Set up the project with 4 management stages: Stage 1. Standard PRINCE2 initiation activities.

Stage 2. Create detailed designs (future organization, processes, systems and operating models) and the service level agreement between MFH and the future service provider.

Stage 3. Request and evaluate proposals, select service provider and agree contract.

Stage 4. Transfer equipment and staff, transfer responsibility for service provision and run trial period.

Initial estimates indicated that the project would cost £2.5m and take two years to complete. MFH senior management agreed that there was a case for outsourcing, and accepted the recommendations as a basis for the project. There is an expected saving of £20m over 10 years.

The Outsourcing project has completed the Starting up a Project process and is now in the initiation stage. Because of the strategic importance of the project, the

MFH Chief Executive Officer has taken the role of Executive. A PRINCE2-experienced Project Manager has been appointed from within MFH. Staff within the business functions being outsourced will work with the external consultants who conducted the feasibility study to define the detailed designs. Which 2 statements should be recorded under the Reasons heading?

- A. The lack of up-to-date technology in MFH means a re-engineering of existing services will not necessarily deliver the performance improvements required.
- B. Providing re-engineered services in-house will remove the need to transfer staff to a service provider.
- C. The Ministry of Food Hygiene (MFH) needs to deal with the increasing pressure to cut costs and better manage supplier's performance.
- D. Relocating staff to the selected service provider's premises will mean that no property transfer is required.
- E. The inadequate controls, outdated standards and outdated technology must be addressed.

Answer: CD

Explanation:

<http://www.whatisprince2.net/prince2-theme-business-case.php>

NEW QUESTION 46

- (Exam Topic 2)

Scenario

A central government department, the Ministry of Food Hygiene (MFH), faces increasing pressure to cut costs, better manage suppliers' performance and reduce the confusion caused by inadequate internal controls, outdated standards and outdated technology. External consultants were employed to conduct a feasibility study to identify options to address the problems, and the likely costs and benefits. The following options were considered:

Do nothing.

Re-engineer selected business functions. Outsource selected business functions.

The feasibility study concluded that there was a case for outsourcing the MFH Information Technology Division and the Facilities Division (maintenance of buildings and grounds). The recommendations were:

One service provider should be contracted to provide the services currently provided by the Information Technology Division and the Facilities Division.

A 10-year service contract should be agreed with the selected service provider.

The feasibility study developed high-level designs of the current organization, processes, systems and operating models, plus an outline Business Case for the required project. The external consultants also made the following recommendations for the management of the project:

Use PRINCE2.

Set up the project with 4 management stages: Stage 1. Standard PRINCE2 initiation activities.

Stage 2. Create detailed designs (future organization, processes, systems and operating models) and the service level agreement between MFH and the future service provider.

Stage 3. Request and evaluate proposals, select service provider and agree contract.

Stage 4. Transfer equipment and staff, transfer responsibility for service provision and run trial period. Initial estimates indicated that the project would cost £2.5m and take two years to complete.

MFH senior management agreed that there was a case for outsourcing, and accepted the recommendations as a basis for the project. There is an expected saving of £20m over 10 years.

The Outsourcing project has completed the Starting up a Project process and is now in the initiation stage. Because of the strategic importance of the project, the MFH Chief Executive Officer has taken the role of Executive. A PRINCE2-experienced Project Manager has been appointed from within MFH. Staff within the business functions being outsourced will work with the external consultants who conducted the feasibility study to define the detailed designs.

Which 2 statements should be recorded under the Expected dis-benefits heading?

- A. An investment of £2.5m is required.
- B. Staff morale will be negatively affected.
- C. The project will take two years to deliver.
- D. Staff may lose the opportunity to work in Information Technology.
- E. MFH will lose direct control over the outsourced business functions.

Answer: CE

NEW QUESTION 47

- (Exam Topic 2)

Which of the following should NOT be included in the business case?

- A. Reasons
- B. Major Risks
- C. Business options
- D. Business approach

Answer: D

NEW QUESTION 48

- (Exam Topic 2)

When considering the business options in the business case, which of these is NOT an option?

- A. Do nothing
- B. Do the maximum
- C. Do the minimum
- D. Do something

Answer: B

NEW QUESTION 52

- (Exam Topic 3)

Which of the following represents the four key characteristics a good Project board should display?

- A. Authority, Credibility, Commitment, Availability
- B. Authority, Credibility, Delegation, Availability

- C. Authority, Availability, Connections, Delegation
- D. Authority, Credibility, Connections, Delegation

Answer: B

NEW QUESTION 53

- (Exam Topic 3)

Who is responsible for ensuring that Communication Management Strategy is appropriate and that planned communication activities actually take place?

- A. Project Assurance
- B. Project Manager
- C. Corporate or Programme Management
- D. Project Support

Answer: A

NEW QUESTION 58

- (Exam Topic 3)

Which of the following roles cannot be combined?

- A. Executive and Senior User
- B. Project Manager and Project Support
- C. Project Assurance and Team Manager
- D. Senior Supplier and Supplier Assurance

Answer: C

NEW QUESTION 59

- (Exam Topic 3)

Scenario

Additional Information

Chief Executive Officer (CEO): He started the company 25 years ago and knows his job very well. He injured his leg two years ago which has restricted his visits to the engineering area. As CEO he has an overall perspective of the business strategic requirements and the authority to commit resources as required.

Marketing Director: She has been with the company for three years, following a successful career with a publicity company. She has the ability to represent the needs of the business, particularly as this is a marketing project. She has the authority to commit the annual business marketing budget, from which the project will be funded, as she sees appropriate. She will be responsible for monitoring the expected benefits of the calendar, in particular the improvement of the company's image.

Engineering Manager: He has been responsible for many engineering innovations in the company and is still as keen and energetic as the day he started. VVhilst he will not be part of the project team, his staff will feature in the photos for the promotional calendar.

Central Records: This group of five staff looks after all company records and document control. They now maintain all project files.

Bright Lights: This is the local office supplies company. It supplies all the stationery and office equipment needs of the company and will supply the stationery for this project.

Portraits Ltd: This is a professional photographic company with a number of excellent photographers and a history of successful work. This company has been selected to take the photos for the company calendar. It has yet be decided which of the photographers to use.

Which 2 statements explain why the Marketing Director should be appointed as the Executive for this project?

- A. She has been with the company for three years.
- B. She previously had a successful career in publicity.
- C. She is able to represent the business needs of MNO Manufacturing.
- D. She has authority to commit the marketing budget, from which the project will be funded.
- E. She requires more experience working with the engineering industry.

Answer: CD

NEW QUESTION 60

- (Exam Topic 3)

Scenario

Additional Information

Chief Executive Officer (CEO): He started the company 25 years ago and knows his job very well. He injured his leg two years ago which has restricted his visits to the engineering area. As CEO he has an overall perspective of the business strategic requirements and the authority to commit resources as required.

Marketing Director: She has been with the company for three years, following a successful career with a publicity company. She has the ability to represent the needs of the business, particularly as this is a marketing project. She has the authority to commit the annual business marketing budget, from which the project will be funded, as she sees appropriate. She will be responsible for monitoring the expected benefits of the calendar, in particular the improvement of the company's image.

Engineering Manager: He has been responsible for many engineering innovations in the company and is still as keen and energetic as the day he started. VVhilst he will not be part of the project team, his staff will feature in the photos for the promotional calendar.

Central Records: This group of five staff looks after all company records and document control. They now maintain all project files.

Bright Lights: This is the local office supplies company. It supplies all the stationery and office equipment needs of the company and will supply the stationery for this project.

Portraits Ltd: This is a professional photographic company with a number of excellent photographers and a history of successful work. This company has been selected to take the photos for the company calendar. It has yet been decided which of the photographers to use.

Which 2 statements explain why the CEO should be appointed as the Executive for this project?

- A. He started the company 25 years ago.
- B. He knows his job very well.
- C. He restricts his visits to the engineering area.
- D. He has the authority to commit resources as required.
- E. He has an overall perspective of the business's strategic requirements.

Answer: DE

NEW QUESTION 65

- (Exam Topic 3)

Which of the following is False?

A Successful project management team should.

- A. Have business, user and supplier stakeholder representation
- B. Never be reviewed as members should stay with the team for the duration
- C. Ensure appropriate governance by defining responsibilities for directing, managing and delivering the project and clearly defining accountability at all levels
- D. Have an effective strategy to manage communication flows to and from stakeholders


Answer: B

NEW QUESTION 67

- (Exam Topic 3)

Scenario

Additional Information

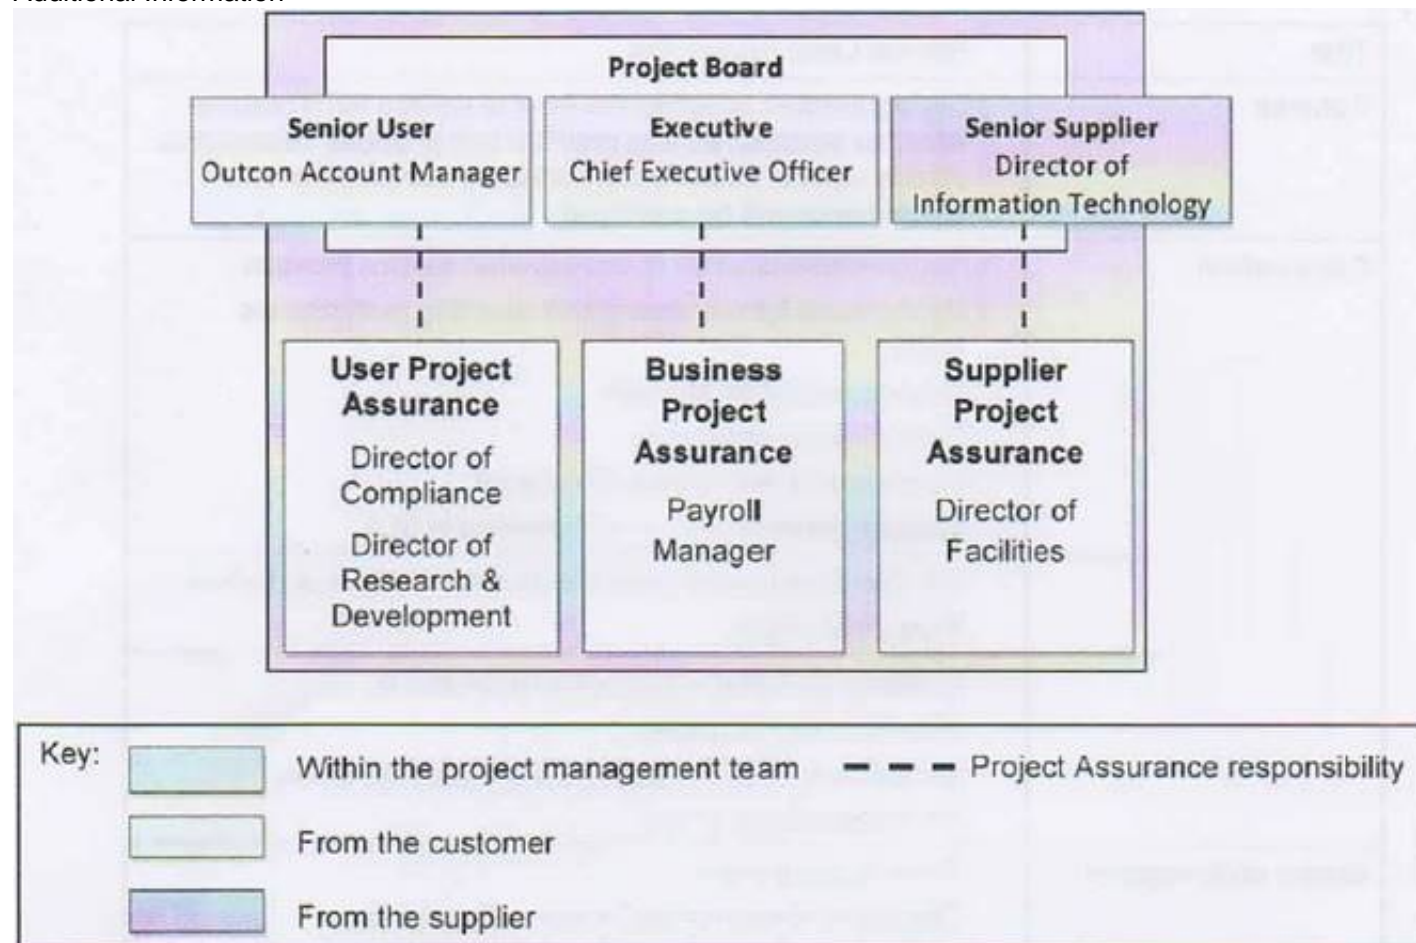

Further information on some resources who could be involved in the project:

Outcome Account Manager: He represents Outcome which is a recruitment agency that provides specialist outsourcing resources. Outcome provided the consultants who carried out the feasibility study and the same consultants will be providing support and guidance to the Information Technology and Facilities teams during the project.

Director of Finance Division: She was transferred from the Information Technology Division 12 months ago. She is responsible for ensuring a cost-conscious approach is adopted in all operational and project activities across the Ministry of Food Hygiene.

Hardware Manager: Reports to the Director of Information Technology. He provides computer hardware to all business functions but has little awareness of the needs of his colleagues working in software.

Payroll Manager: Reports to the Director of Finance. He is a very experienced and efficient qualified accountant who has much of the responsibility of running the Finance Division on behalf of the Director of Finance. He has been involved in drafting the Ministry's business strategy and assisting in a full business risk assessment. He also drafted the corporate Business Case standards.

Which 2 alternative actions apply to the proposed user assurance for this project?

- A. Retain because they are both very positive about outsourcing the selected business functions.
- B. Retain because their divisions will be the major users of the outsourced services and they can provide the user perspective on the impact of any proposed changes.
- C. Remove because neither of these individuals are from the business functions to be outsourced.
- D. Retain because selecting only one of them may cause unnecessary conflict.
- E. Retain because they are able to help identify stakeholders and their communication requirements.


Answer: BE

NEW QUESTION 68

- (Exam Topic 3)

Scenario

Additional Information

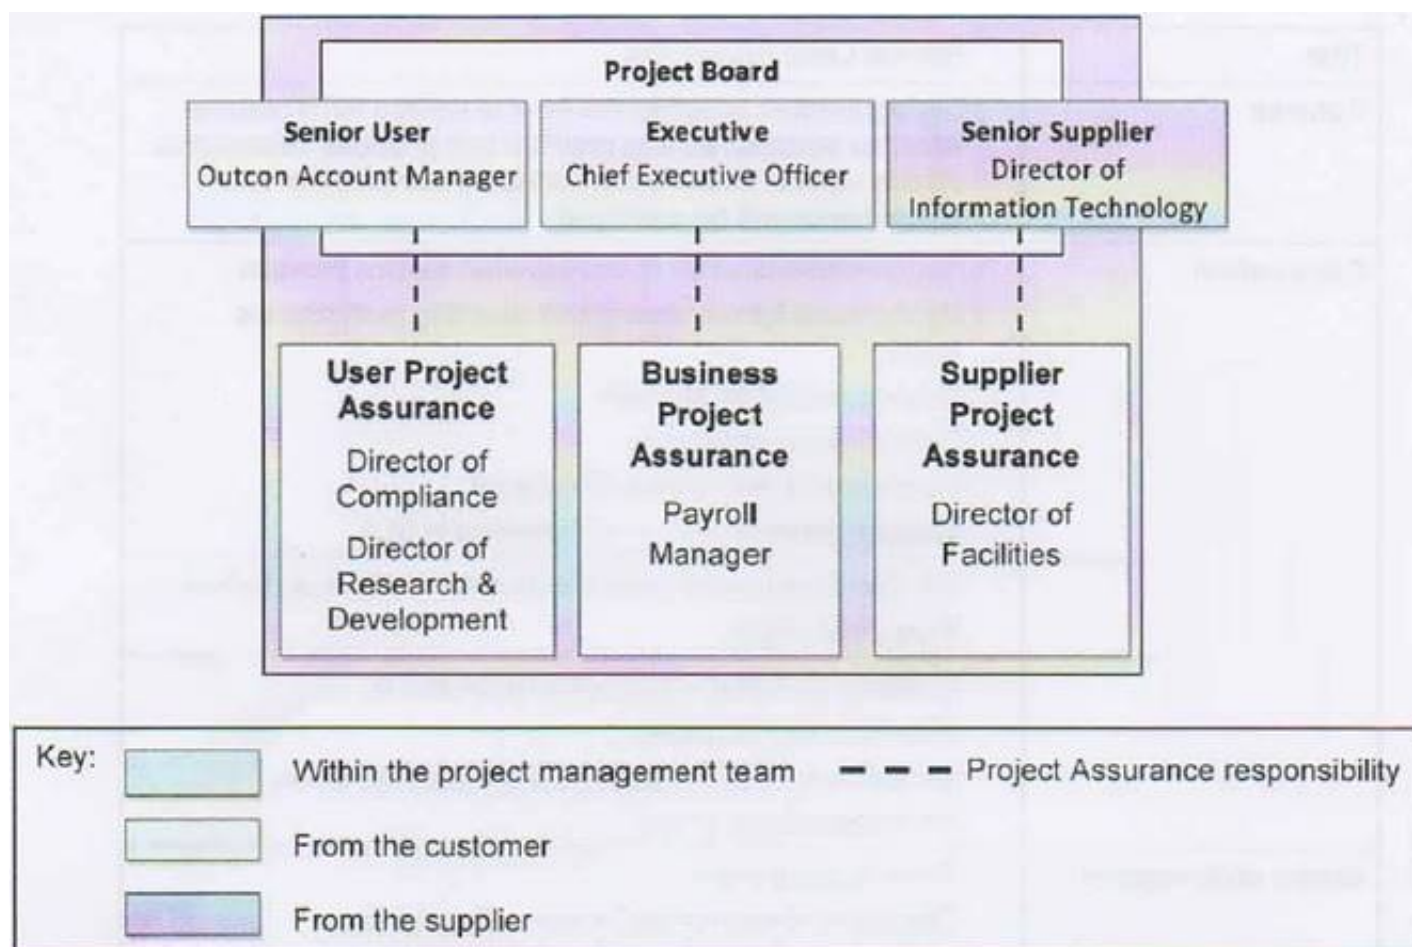

Further information on some resources who could be involved in the project:

Outcome Account Manager: He represents Outcome which is a recruitment agency that provides specialist outsourcing resources. Outcome provided the consultants who carried out the feasibility study and the same consultants will be providing support and guidance to the Information Technology and Facilities teams during the project.

Director of Finance Division: She was transferred from the Information Technology Division 12 months ago. She is responsible for ensuring a cost-conscious approach is adopted in all operational and project activities across the Ministry of Food Hygiene.

Hardware Manager: Reports to the Director of Information Technology. He provides computer hardware to all business functions but has little awareness of the needs of his colleagues working in software.

Payroll Manager: Reports to the Director of Finance. He is a very experienced and efficient qualified accountant who has much of the responsibility of running the Finance Division on behalf of the Director of Finance. He has been involved in drafting the Ministry's business strategy and assisting in a full business risk assessment. He also drafted the corporate Business Case standards.

Which 2 alternative actions apply to the proposed supplier assurance for this project?

- A. Retain because he has a professional facilities qualification and so is in a position to specify the needs of his division.
- B. Retain because he will be able to advise on many of the products that will enable outsourcing to happen, such as the 10-year outsourcing service contract.
- C. Retain because he is well-regarded within the Ministry because of the efficiencies, superb service and savings he has achieved in the Facilities Division.
- D. Add 'Outcome Account Manager' because he will advise on potential changes and their impact on the integrity of the project's products.
- E. Remove because he is involved with the project and is therefore NOT independent.

Answer: BD

NEW QUESTION 71

- (Exam Topic 3)

Additional Information

Chief Executive Officer (CEO): He started the company 25 years ago and knows his job very well. He injured his leg two years ago which has restricted his visits to the engineering area. As CEO he has an overall perspective of the business strategic requirements and the authority to commit resources as required.

Marketing Director: She has been with the company for three years, following a successful career with a publicity company. She has the ability to represent the needs of the business, particularly as this is a marketing project. She has the authority to commit the annual business marketing budget, from which the project will be funded, as she sees appropriate. She will be responsible for monitoring the expected benefits of the calendar, in particular the improvement of the company's image.

Engineering Manager: He has been responsible for many engineering innovations in the company and is still as keen and energetic as the day he started. Whilst he will not be part of the project team, his staff will feature in the photos for the promotional calendar.

Central Records: This group of five staff looks after all company records and document control. They now maintain all project files.

Bright Lights: This is the local office supplies company. It supplies all the stationery and office equipment needs of the company and will supply the stationery for this project.

Portraits Ltd: This is a professional photographic company with a number of excellent photographers and a history of successful work. This company has been selected to take the photos for the company calendar. It has yet to be decided which of the photographers to use.

Using the additional Information provided for this question In the Scenario Booklet, answer the following question.

Lines 1 to 5 in the table below consist of an assertion statement and a reason statement. For each line identify the appropriate option, from options A to E, that applies. Each option can be used once, more than once or not at all.

	Assertion	True False	Reason	
A	The Executive role should be shared by the CEO and the Marketing Director.	True False	The Executive is responsible for securing the funding for the project.	True False
B	The Senior User role should be shared by the Marketing Director and the Engineering Manager.	True False	Those who provide specialist resources to the project development teams should perform a Senior User role.	True False
C	Although Bright Lights and Portraits Ltd are suppliers, they CANNOT both perform a Senior Supplier role on this project.	True False	When the Senior Supplier role is shared between two suppliers, one of the suppliers must be internal to the business.	True False
D	A single member of Central Records should NOT perform both a Project Support and a Project Assurance role on this project.	True False	It is necessary to keep Project Support and Project Assurance responsibilities separate.	True False
E	The Engineering Manager should be included in the Communication Management Strategy.	True False	The Communication Management Strategy describes the communication tools to be used.	True False

- A. Mastered
B. Not Mastered

Answer: A

Explanation:

	Assertion	True False	Reason	
A	The Executive role should be shared by the CEO and the Marketing Director.	True - False	The Executive is responsible for securing the funding for the project.	True - False
B	The Senior User role should be shared by the Marketing Director and the Engineering Manager.	True - False	Those who provide specialist resources to the project development teams should perform a Senior User role.	True - False
C	Although Bright Lights and Portraits Ltd are suppliers, they CANNOT both perform a Senior Supplier role on this project.	True - False	When the Senior Supplier role is shared between two suppliers, one of the suppliers must be internal to the business.	True - False
D	A single member of Central Records should NOT perform both a Project Support and a Project Assurance role on this project.	True - False	It is necessary to keep Project Support and Project Assurance responsibilities separate.	True - False
E	The Engineering Manager should be included in the Communication Management Strategy.	True - False	The Communication Management Strategy describes the communication tools to be used.	True - False

NEW QUESTION 74

- (Exam Topic 3)

Scenario

Additional Information

Chief Executive Officer (CEO): He started the company 25 years ago and knows his job very well. He injured his leg two years ago which has restricted his visits to the engineering area. As CEO he has an overall perspective of the business strategic requirements and the authority to commit resources as required.

Marketing Director: She has been with the company for three years, following a successful career with a publicity company. She has the ability to represent the needs of the business, particularly as this is a marketing project. She has the authority to commit the annual business marketing budget, from which the project will be funded, as she sees appropriate. She will be responsible for monitoring the expected benefits of the calendar, in particular the improvement of the company's image.

Engineering Manager: He has been responsible for many engineering innovations in the company and is still as keen and energetic as the day he started. Whilst he will not be part of the project team, his staff will feature in the photos for the promotional calendar.

Central Records: This group of five staff looks after all company records and document control. They now maintain all project files.

Bright Lights: This is the local office supplies company. It supplies all the stationery and office equipment needs of the company and will supply the stationery for this project.

Portraits Ltd: This is a professional photographic company with a number of excellent photographers and a history of successful work. This company has been selected to take the photos for the company calendar. It has yet to be decided which of the photographers to use.

Which 2 statements explain why Central Records should be appointed as Project Support for this project?

- A. They control the receipt, identification, versions, storage and issue of all project products within the company's projects.
- B. They already exist within the organization and have been with the company for many years.
- C. They will ensure compliance with all company policies and procedures.
- D. They perform a quality assurance function across all projects.
- E. They have knowledge of the organizational standards that will be applicable to the project.

Answer: AE

NEW QUESTION 77

- (Exam Topic 4)

Scenario

Extract from the Project Product Description (with errors)

Composition	1. Monthly calendar displays 2. 100gsm glossy paper 3. Full colour 4. Selected envelope 5. Chosen label design 6. List of customers 7. Selected photos 8. Photo session schedule
Derivation	9. New company logo design 10. Previous calendar designs 11. Internal creative team 12. Production cost forecast
Development skills required	13. Photographer 14. Internal creative team 15. Printer
Customer's quality expectations	16. Professional photos 17. 10% more calendars should be printed than required to allow for any late additions to the list of customers 18. Compliance with applicable corporate standards 19. The calendar should reflect the company image as described in the corporate branding standards 20. The calendar will increase orders by at least 10% with a minimum of 10 further orders from the list of prospective customers within 12 months
Acceptance criteria	21. Appearance - each photo should be sufficiently attractive and humorous that the customer wants to display it 22. Appearance - new company logo promotes strong image 23. Security - complies with Data Protection Act 24. Accuracy - public holidays match the list supplied by Marketing on 01 November

Which 2 statements apply to the Acceptance criteria section?

- A. Amend entry 21 to 'Appearance - 12 photos each showing different members of staff.
- B. Move entry 21 to Composition because the photos are part of the final product.
- C. Delete entry 22 because the development of the new company logo is not within the scope of the Calendar project.
- D. Move entry 23 to Derivation because the Data Protection Act already exists.
- E. Delete entry 24 because this is NOT a suitable acceptance criteria for this project.

Answer: AC

NEW QUESTION 82

- (Exam Topic 4)

Scenario

Additional Information Product Description

Title	Service Level Agreement.
Purpose	<ul style="list-style-type: none"> This agreement specifies the level of service MFH requires from the selected service provider and provides measurable criteria against which the selected service provider's performance will be assessed.
Composition	<ul style="list-style-type: none"> Responsibilities of MFH and selected service provider. Mechanisms for monitoring and reporting performance levels. Dispute resolution process. Confidentiality provisions. Conditions for termination of contract. Glossary of technical terms contained in SLA.
Format and presentation	<ul style="list-style-type: none"> A4, Word document, printed both sides in black and white. Font: Arial, 12pts.
Quality criteria	<ul style="list-style-type: none"> Contains all composition items listed above. Not more than 60 pages. Complies with MFH corporate branding standards. No typographical errors.
Quality skills required	<ul style="list-style-type: none"> Proof-reading skills. Director of Compliance Division - Reviewer. Director of Information Technology Division - Reviewer. Administrator.
Quality responsibilities	<ul style="list-style-type: none"> Producer/Presenter: Director of Facilities Division. Chair: Project Manager.

Quality notes from the Daily Log

The Director of Information Technology Division (DIT) has been asked to ensure that any changes to the outsourced staff employment contracts adhere to employment law. The DIT will review future job descriptions of the transferred staff before the final contract is signed with the selected service provider. The service level agreement between MFH and the selected service provider will specify the type and quality of service required. The selected service provider must follow the industry standards for providing outsourced services.

MFH has a quality management system which contains a document control procedure for all its documentation, however this does not include change management.

All project documents will be subject to a quality review. Nominated products will require a formal approval record signed-off by the quality review chair.

Extract from the draft Quality Management Strategy (may contain errors) Introduction

- * 1. This document defines the approach to be taken to achieve the required quality levels during the project.
- * 2. The Project Board will have overall responsibility for the Quality Management Strategy.
- * 3. Project Assurance will provide assurance on the implementation of the Quality Management Strategy. Quality management procedure - Quality standards
- * 4. The selected service provider will operate to industry standards for providing outsourced services.
- * 5. MFH document standards will be used. Records
- * 6. A Quality Register will be maintained to record the planned quality events and the actual results from the quality activities.
- * 7. Configuration Item Records will be maintained for each product to describe its status, version and variant.
- * 8. Approval records for products that require them will be stored in the quality database. Roles and responsibilities
- * 9. The DIT will check that the employment contracts for outsourced staff adhere to employment law.
- * 10. Team Managers will provide details of quality checks that have been carried out.
- * 11. Team Managers will ensure that the Quality Register is updated with the names of team members who are involved in the review process.
- * 12. The Senior User will review the Product Descriptions of the products to be produced by the selected service provider to ensure that they can be achieved.

Which is a correctly defined acceptance criterion for the transferred facilities computer system?

- A. Must be subject to regular back-ups.
- B. Planned periods of shutdowns of the computer system must be kept to a minimum.
- C. No (zero) loss of system functionality.
- D. Back-up of data must be kept until the data is no longer needed.

Answer: C

NEW QUESTION 86

- (Exam Topic 4)

Scenario

Additional Information Product Description

Title	Service Level Agreement.
Purpose	<ul style="list-style-type: none"> This agreement specifies the level of service MFH requires from the selected service provider and provides measurable criteria against which the selected service provider's performance will be assessed.
Composition	<ul style="list-style-type: none"> Responsibilities of MFH and selected service provider. Mechanisms for monitoring and reporting performance levels. Dispute resolution process. Confidentiality provisions. Conditions for termination of contract. Glossary of technical terms contained in SLA.
Format and presentation	<ul style="list-style-type: none"> A4, Word document, printed both sides in black and white. Font: Arial, 12pts.
Quality criteria	<ul style="list-style-type: none"> Contains all composition items listed above. Not more than 60 pages. Complies with MFH corporate branding standards. No typographical errors.
Quality skills required	<ul style="list-style-type: none"> Proof-reading skills. Director of Compliance Division - Reviewer. Director of Information Technology Division - Reviewer. Administrator.
Quality responsibilities	<ul style="list-style-type: none"> Producer/Presenter: Director of Facilities Division. Chair: Project Manager.

Quality notes from the Daily Log

The Director of Information Technology Division (DIT) has been asked to ensure that any changes to the outsourced staff employment contracts adhere to employment law. The DIT will review future job descriptions of the transferred staff before the final contract is signed with the selected service provider. The service level agreement between MFH and the selected service provider will specify the type and quality of service required. The selected service provider must follow the industry standards for providing outsourced services.

MFH has a quality management system which contains a document control procedure for all its documentation, however this does not include change management.

All project documents will be subject to a quality review. Nominated products will require a formal approval record signed-off by the quality review chair.

Extract from the draft Quality Management Strategy (may contain errors) Introduction

- * 1. This document defines the approach to be taken to achieve the required quality levels during the project.
- * 2. The Project Board will have overall responsibility for the Quality Management Strategy.
- * 3. Project Assurance will provide assurance on the implementation of the Quality Management Strategy. Quality management procedure - Quality standards
- * 4. The selected service provider will operate to industry standards for providing outsourced services.
- * 5. MFH document standards will be used. Records
- * 6. A Quality Register will be maintained to record the planned quality events and the actual results from the quality activities.
- * 7. Configuration Item Records will be maintained for each product to describe its status, version and variant.
- * 8. Approval records for products that require them will be stored in the quality database. Roles and responsibilities
- * 9. The DIT will check that the employment contracts for outsourced staff adhere to employment law.
- * 10. Team Managers will provide details of quality checks that have been carried out.
- * 11. Team Managers will ensure that the Quality Register is updated with the names of team members who are involved in the review process.
- * 12. The Senior User will review the Product Descriptions of the products to be produced by the selected service provider to ensure that they can be achieved.

None of the reviewers have proof-reading skills.

- A. Record an action to request that Project Assurance identify a proof-reader who can, within the next 2 days, complete the check for typographical errors.
- B. Ask the reviewers present at the meeting to conduct a proof-reading exercise and pass any comments to the author within 2 days.
- C. Contact Project Assurance to find appropriate resources to come into the review.
- D. No action required.

Answer: A

NEW QUESTION 87

.....

THANKS FOR TRYING THE DEMO OF OUR PRODUCT

Visit Our Site to Purchase the Full Set of Actual PRINCE2-Practitioner Exam Questions With Answers.

We Also Provide Practice Exam Software That Simulates Real Exam Environment And Has Many Self-Assessment Features. Order the PRINCE2-Practitioner Product From:

<https://www.2passeasy.com/dumps/PRINCE2-Practitioner/>

Money Back Guarantee

PRINCE2-Practitioner Practice Exam Features:

- * PRINCE2-Practitioner Questions and Answers Updated Frequently
- * PRINCE2-Practitioner Practice Questions Verified by Expert Senior Certified Staff
- * PRINCE2-Practitioner Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PRINCE2-Practitioner Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year
